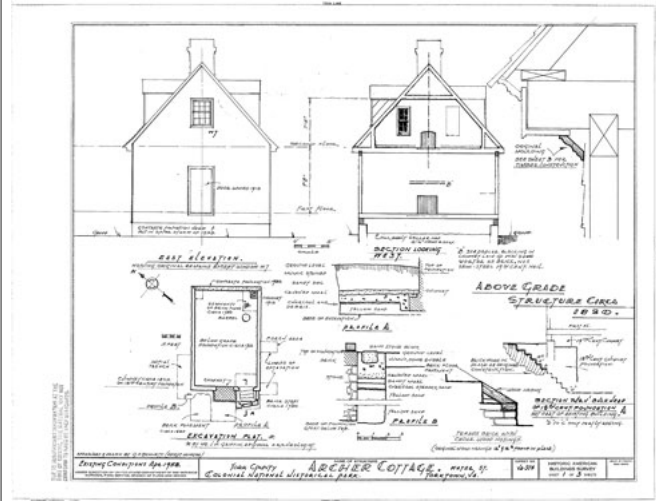


T	Key	Summary	P	Status	Planned Start	Planned End	Description
Task	OB-1	General Conditions	Critical	In Progress	02/Jan/12	25/Jan/12	Documentation should be attached
Sub-task	OB-2	OB-1 Finalize the plans and develop estimate with owner, architect	Major	Open	02/Jan/12	20/Jan/12	<ul style="list-style-type: none"> Develop conceptual floor plan Rough draft typical wall sections with finishes desired by Owner. Determine roof structure and roof materials desired or acceptable as options by owner. Prepare preliminary site play layout. (Conceptual) Based on recommendations, develop secondary site plan (pre-design) site plan. Determine the following architectural options/needs with owner. <ol style="list-style-type: none"> Desired interior finishes H.V.A.C. options Special lighting Special equipment Special accessories Electrical service equipment
Sub-task	OB-3	OB-1 Sign contract and notice to proceed	Blocker	Closed	23/Jan/12	25/Jan/12	
Task	OB-4	Site work	Major	In Progress	25/Jan/12	27/Jan/12	See the drawing:  <p>The drawing is a detailed architectural site plan for 'Archer Cottage'. It includes a 'WEST ELEVATION' and a 'SECTION THROUGH WEST WALL'. The site plan shows the building footprint, a 'STRUCTURE CIRCLE', and various annotations for site work, including 'EXCAVATION PLAN', 'GRADE', and 'STRUCTURE CIRCLE'. The drawing is signed 'Archer Cottage' and includes a title block with project details.</p>
Sub-task	OB-5	OB-4 Clear and grub lot	Trivial	In Progress	25/Jan/12	25/Jan/12	
Sub-task	OB-6	OB-4 Install temporary power service	Trivial	In Progress	26/Jan/12	26/Jan/12	
Sub-task	OB-7	OB-4 Install underground utilities	Trivial	Open	27/Jan/12	27/Jan/12	
Task	OB-8	Foundation	Major	Open	01/Feb/12	30/Mar/12	
Sub-task	OB-9	OB-8 Excavate for foundations	Major	Open	01/Feb/12	10/Feb/12	
Sub-task	OB-10	OB-8 Form basement walls	Minor	Open	13/Feb/12	16/Feb/12	
Sub-task	OB-11	OB-8 Place concrete for foundations & basement walls	Minor	Open	17/Feb/12	21/Feb/12	
Sub-task	OB-12	OB-8 Cure basement for 7 days	Minor	Open	21/Feb/12	28/Feb/12	
Sub-task	OB-13	OB-8 Strip basement wall forms	Minor	Open	29/Feb/12	29/Feb/12	

T	Key	Summary	P	Status	Planned Start	Planned End	Description
Sub-task	OB-14	OB-8 Waterproof/insulate basement walls	Minor	Open	01/Mar/12	06/Mar/12	
Sub-task	OB-16	OB-8 Backfill foundations	Minor	Open	07/Mar/12	30/Mar/12	
Sub-task	OB-15	OB-8 Perform foundation inspection	Minor	Open	07/Mar/12	07/Mar/12	
Task	OB-17	Framing	Major	Open	02/Apr/12	27/Apr/12	
Sub-task	OB-18	OB-17 Install 1st floor joists	Minor	Open	02/Apr/12	03/Apr/12	
Sub-task	OB-19	OB-17 Lay 1st floor decking	Minor	Open	04/Apr/12	05/Apr/12	
Sub-task	OB-20	OB-17 Frame 1st floor walls	Minor	Open	06/Apr/12	09/Apr/12	
Sub-task	OB-21	OB-17 Frame 1st floor corners	Minor	Open	10/Apr/12	11/Apr/12	
Sub-task	OB-22	OB-17 Install 2nd floor joists	Minor	Open	12/Apr/12	13/Apr/12	
Sub-task	OB-23	OB-17 Frame 2nd floor decking	Minor	Open	16/Apr/12	17/Apr/12	
Sub-task	OB-24	OB-17 Frame 2nd floor walls	Minor	Open	18/Apr/12	19/Apr/12	
Sub-task	OB-25	OB-17 Frame 2nd floor corners	Minor	Open	20/Apr/12	23/Apr/12	
Sub-task	OB-26	OB-17 Complete roof framing	Minor	Open	24/Apr/12	25/Apr/12	
Sub-task	OB-27	OB-17 Conduct framing inspection	Major	Open	26/Apr/12	30/Apr/12	
Task	OB-31	Utility Rough-ins and Complete Concrete	Major	Open	01/May/12	31/May/12	
Sub-task	OB-32	OB-31 Rough-in plumbing	Minor	Open	07/May/12	11/May/12	
Sub-task	OB-35	OB-31 Rough-in electricals	Minor	Open	08/May/12	10/May/12	
Sub-task	OB-36	OB-31 Conduct rough-in electrical inspection	Minor	Open	11/May/12	11/May/12	
Sub-task	OB-34	OB-31 Place concrete for basement floor	Minor	Open	14/May/12	18/May/12	
Sub-task	OB-33	OB-31 Conduct rough-in plumbing inspection	Minor	Open	14/May/12	15/May/12	
Sub-task	OB-37	OB-31 Rough-in HVAC	Minor	Open	22/May/12	24/May/12	
Sub-task	OB-38	OB-31 Conduct rough-in HVAC inspection	Minor	Open	25/May/12	28/May/12	
Sub-task	OB-39	OB-31 Rough-in communication - phone, cable, computer, alarm	Minor	Open	25/May/12	25/May/12	
Task	OB-28	Exterior finishes	Major	Open	28/May/12	29/Jun/12	
Sub-task	OB-29	OB-28 Complete exterior brick	Major	Open	28/May/12	15/Jun/12	
Sub-task	OB-30	OB-28 Complete exterior siding	Minor	Open	18/Jun/12	29/Jun/12	
Task	OB-40	Interior Finishes	Major	Open	02/Jul/12	30/Jul/12	
Sub-task	OB-41	OB-40 Place wall insulation - 1st floor	Minor	Open	02/Jul/12	02/Jul/12	
Sub-task	OB-42	OB-40 Place wall insulation - 2nd floor	Minor	Open	03/Jul/12	03/Jul/12	
Sub-task	OB-43	OB-40 Place ceiling insulation - 2nd floor	Minor	Open	04/Jul/12	04/Jul/12	
Sub-task	OB-44	OB-40 Conduct insulation inspection	Minor	Open	05/Jul/12	05/Jul/12	
Sub-task	OB-45	OB-40 Install drywall - 1st floor walls	Minor	Open	09/Jul/12	09/Jul/12	

T	Key	Summary	P	Status	Planned Start	Planned End	Description
Sub-task	OB-46	OB-40 Install drywall 2nd floor walls	Minor	Open	10/Jul/12	10/Jul/12	
Sub-task	OB-47	OB-40 Tape and float 1st floor drywall	Minor	Open	11/Jul/12	12/Jul/12	
Sub-task	OB-48	OB-40 Tape and float 2nd floor drywall	Minor	Open	13/Jul/12	16/Jul/12	
Sub-task	OB-49	OB-40 Texture all	Major	Open	17/Jul/12	20/Jul/12	
Sub-task	OB-50	OB-40 Paint all	Major	Open	23/Jul/12	27/Jul/12	
Sub-task	OB-51	OB-40 Paint exterior siding & trim work	Minor	Open	30/Jul/12	30/Jul/12	
Sub-task	OB-52	OB-40 Complete 1st floor plumbing	Minor	Open	31/Jul/12	03/Aug/12	
Sub-task	OB-53	OB-40 Complete 2nd floor - hall bath and private bath plumbing	Minor	Open	06/Aug/12	08/Aug/12	
Sub-task	OB-54	OB-40 Conduct finish plumbing inspection	Minor	Open	10/Aug/12	10/Aug/12	
Sub-task	OB-55	OB-40 Tile entry, kitchen and baths	Minor	Open	13/Aug/12	17/Aug/12	
Sub-task	OB-56	OB-40 Install appliances	Minor	Open	20/Aug/12	20/Aug/12	
Task	OB-57	Landscaping and Grounds Work	Major	Open	27/Aug/12	05/Sep/12	
Sub-task	OB-58	OB-57 Pour concrete driveway and sidewalks	Minor	Open	27/Aug/12	29/Aug/12	
Sub-task	OB-59	OB-57 Install backyard fence	Minor	Open	30/Aug/12	31/Aug/12	
Sub-task	OB-60	OB-57 Sod and complete plantings	Minor	Open	03/Sep/12	05/Sep/12	
Task	OB-61	Final Acceptance	Major	Open	10/Sep/12	21/Sep/12	
Sub-task	OB-62	OB-61 Complete final inspection for certificate of occupancy	Trivial	Open	10/Sep/12	10/Sep/12	
Sub-task	OB-63	OB-61 Cleanup for occupancy	Trivial	Open	11/Sep/12	11/Sep/12	
Sub-task	OB-64	OB-61 Perform final walk-through inspection	Major	Open	12/Sep/12	12/Sep/12	
Sub-task	OB-65	OB-61 Complete punch list items	Critical	Open	13/Sep/12	21/Sep/12	
